

Dunkettle Progress Update


25th November 2022



Twitter



Website

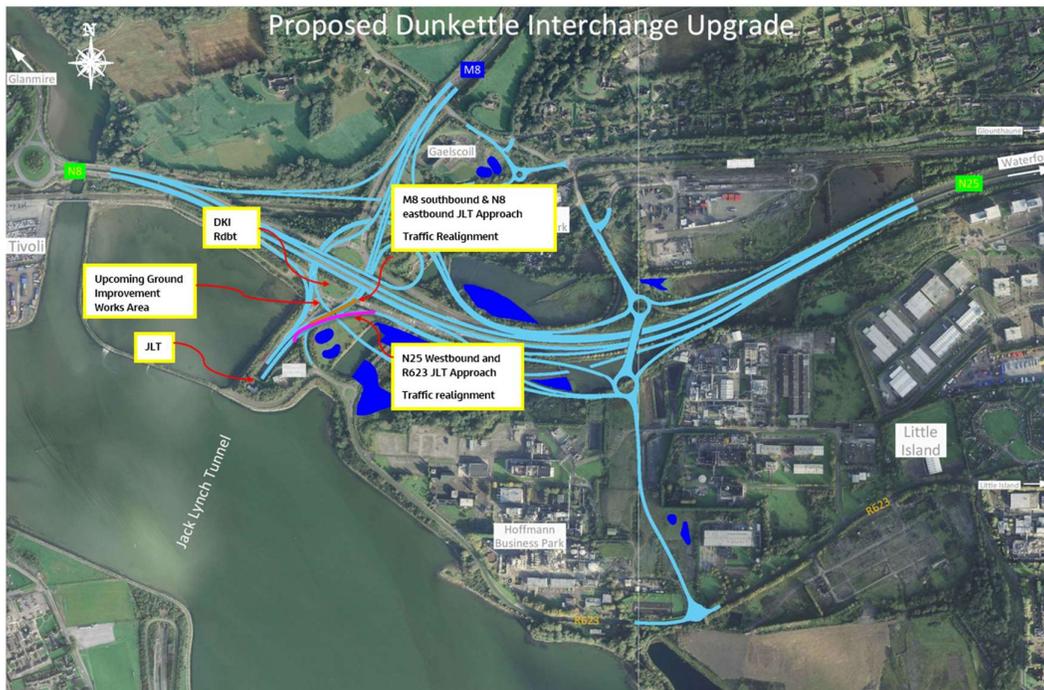

- Following on from the opening of a number of link roads on Sunday 20/11/2022, the new layout has become established and motorists are again reminded that speed control measures will remain on site for the foreseeable future.

- As noted in our previous update, a scale model of the Scheme is available for viewing at the site office in Inchera, Little Island. Please call 1800 810077 (at any time) to arrange a viewing or simply call into the site office during working hours - see photograph below.




Dunkettle Interchange Upgrade Scheme Scale Model.


- A number of minor changes to the alignment will be progressed before the Christmas break. The first of these will be a change in alignment for the M8 southbound, N8 eastbound and the N25 westbound traffic wishing to enter the Jack Lynch Tunnel - see aerial photographs below marked up to illustrate the new routes.
- We hope to complete the realignment under night-time working on the night of Monday the 28th of November 2022. We will issue a short update on Monday the 28th of November 2022 to confirm the same. The realignment works are being progressed under night-time working to minimise the impact to traffic.
- This new layout will be in place for a number of months and will necessitate the installation of additional traffic lights as shown in the photographs below. These will duplicate the existing traffic lights and will not impact on traffic flow.



Traffic entering the Jack Lynch Tunnel from the N25 Westbound diverge.

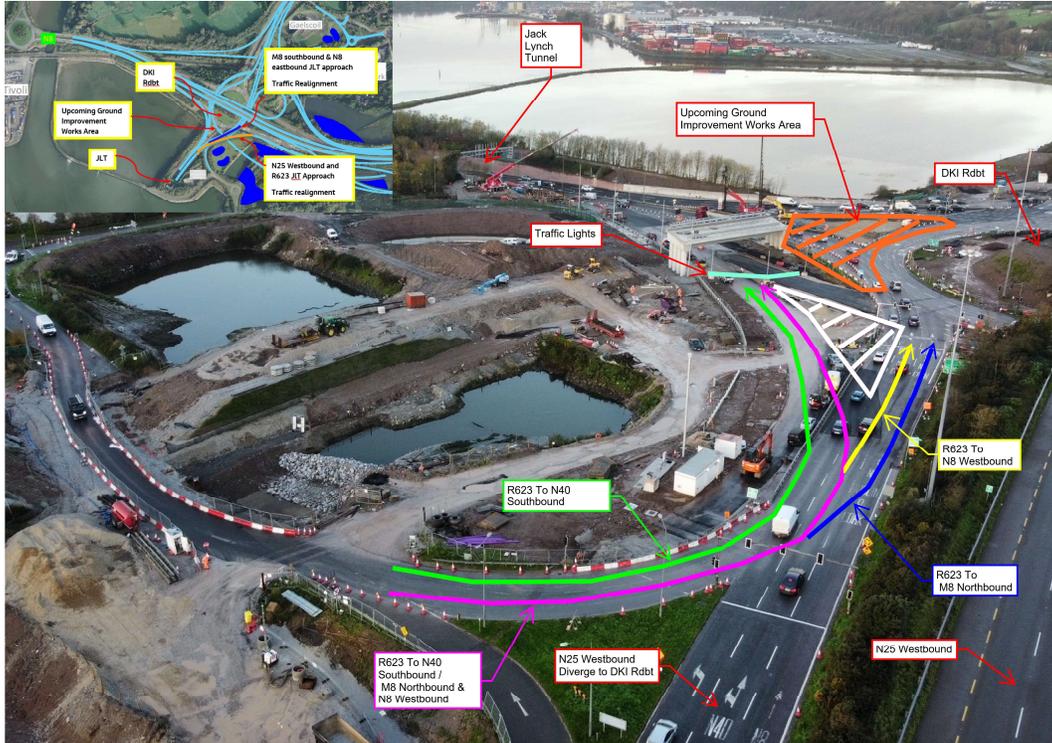


Traffic entering the Jack Lynch Tunnel from the R623.

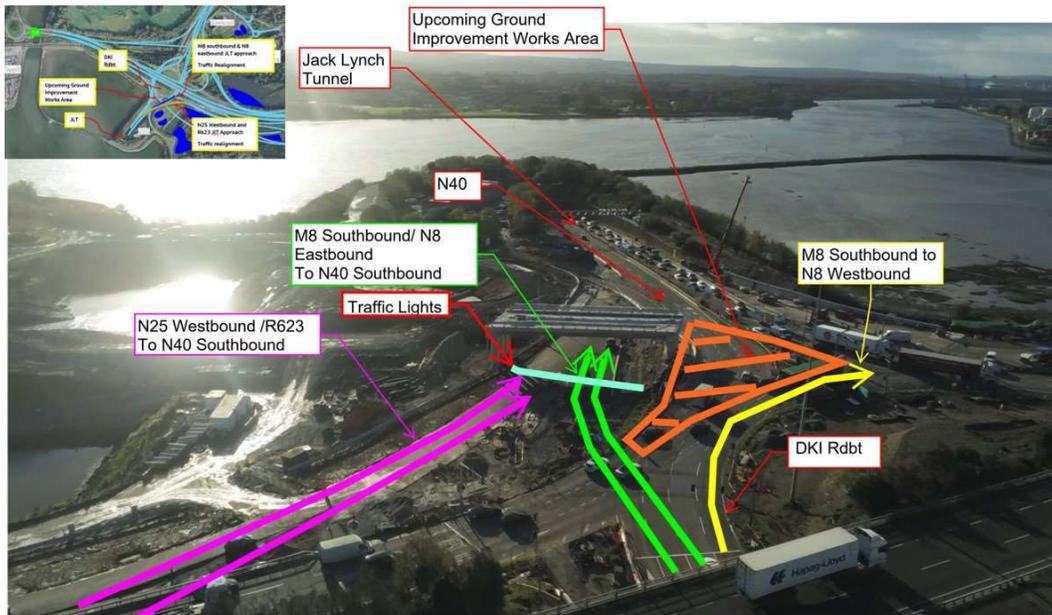

Traffic entering the Jack Lynch Tunnel from the M8 Southbound/N8 Eastbound.

- The purpose of this realignment is to allow us to progress ground improvement works and embankment construction in the area west of Structure St05 which was previously part of the roundabout circulating carriageway and the N40. The immediate works area is shown hereunder in the aerial photograph below. The ground improvement element will continue until Christmas, with embankment construction commencing in January 2023.
- We also intend to carry out piling works in the area shown in the photograph below before Christmas. These works will be progressed under night-time working in order to minimise disruption to traffic.

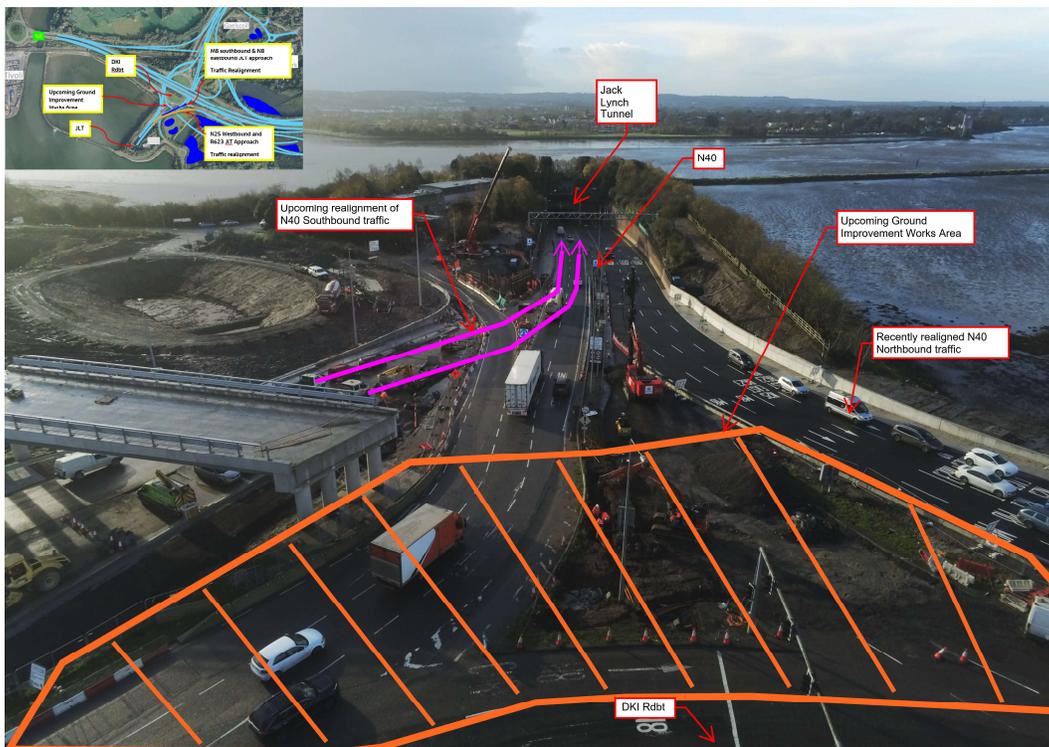


Ground Improvement Works to be progressed west of Structure St05.

The video below shows the route for traffic heading Northbound on the N40 through the Jack Lynch Tunnel wishing to access Little Island.



Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)

As always, if there are any queries or comments in relation to these works, please contact us at:
Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.



Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).
